



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

September 28th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Roof at the new offices area is expected to be complete by the end of the week
- Mechanical mezzanine and stage craft slab is expected to be poured by the end of the week
- Wall framing at auditorium lobby continues
- Exterior stud framing is expected to be complete by the end of the week
- Laying of brick is ongoing from east to west
- Seat risers are in progress
- MEP rough in activities continue

2nd Floor East Renovation (3/17 - 8/17)

- Electrical inspections to be complete by the end of the week
- Overhead doors installation is expected to be complete by the end of the week

Gym Addition (4/17 - 6/18)

- Framing of the soffits continue
- Structural framing is ongoing

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will continue throughout the rest of the auditorium
- Exterior framing and sheathing will continue
- Framing of interior walls will continue

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs work to begin in the next couple weeks
- Slab on grade at the lobby is expected to be poured next week

2nd Floor East Renovation (3/17 - 8/17)

- Ceiling tile to be installed early next week
- Elevator replacement activities are ongoing
- Electrical inspection is expected to occur next week
- Carpet flooring installation to begin early next week

MILESTONE DATES:


- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Exterior Auditorium Framing



Auditorium Seating Progress

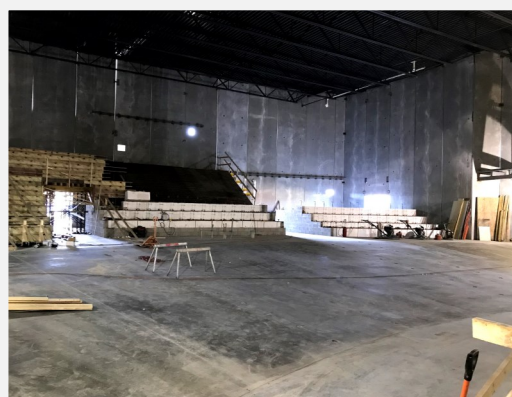

Poured Slab in Auditorium
