



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

January 5th, 2018



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school. The current main entrance will not be available for use starting on January 2nd. All students and staff to use the new main entrance.

MILESTONE DATES:

- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 3/18)

- New front entrance opened last week
- Ceiling clouds installation in the lobby is ongoing
- Painting of auditorium stage is ongoing
- Installation of plywood for wall paneling is ongoing

Gym Addition (4/17 - 6/18)

- Wall framing at lobby is in progress
- Wall framing in locker rooms is ongoing
- Above ceiling rough-ins will continue
- Connectors between the existing building and the new gym is in progress

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 3/18)


- Exterior wall panels installation will resume weather permitting
- Drywall, taping, and finishing will follow once the ceiling clouds in the lobby and north corridors have been complete
- Auditorium wall panels will be installed next week
- Theatrical rigging preparation will begin next week
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will continue in main auditorium
- Ceiling clouds installation in the main auditorium will begin in a couple weeks

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Connectors between the existing building and new gym will continue



Orchestra Pit Progress

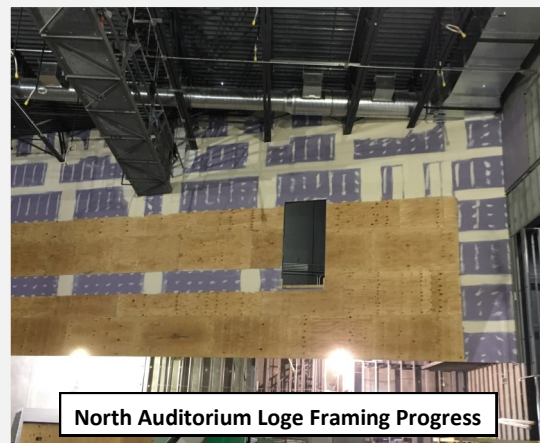

North Auditorium Loge Framing Progress



Auditorium Stage Progress
