



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

January 25th, 2018



CGSCHMIDT<sup>INC.</sup>

## SAFETY:

**Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school. The current main entrance will not be available for use starting on January 2nd. All students and staff to use the new main entrance.**

## MILESTONE DATES:

- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat

## PROGRESS THIS WEEK:

### Auditorium Addition (3/6 - 3/18)

- Wood wall panels installation is ongoing
- Ceiling clouds installation is ongoing
- Theatrical rigging installation started this week
- Taping and finishing of lobby walls is ongoing

### Gym Addition (4/17 - 6/18)

- Wall framing at lobby is in progress
- Basketball hoops installation began earlier this week
- Detail painting is ongoing
- Ductwork installation in mechanical room is ongoing
- Masonry walls at new gym corridor connectors is ongoing

## GOALS NEXT 2 WEEKS:

### Auditorium Addition (3/6 - 3/18)


- Exterior wall panels installation will resume weather permitting
- Auditorium wall panels will continue
- Theatrical rigging installation to be complete by the end of next week
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will continue in main auditorium
- Ceiling clouds installation in the main auditorium will be complete by the end of next week
- Seating to arrive onsite next week
- Painting of raised seating to occur next week

### Gym Addition (4/17 - 6/18)


- Permanent heat to be in place next week
- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Structural steel to be installed in the next couple weeks at new gym corridor connectors



Gym Progress

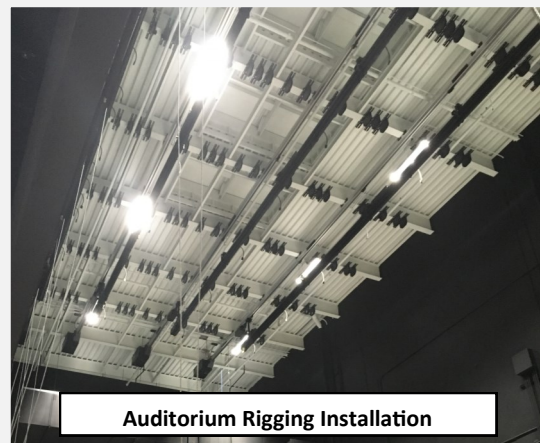

Auditorium Rigging Installation

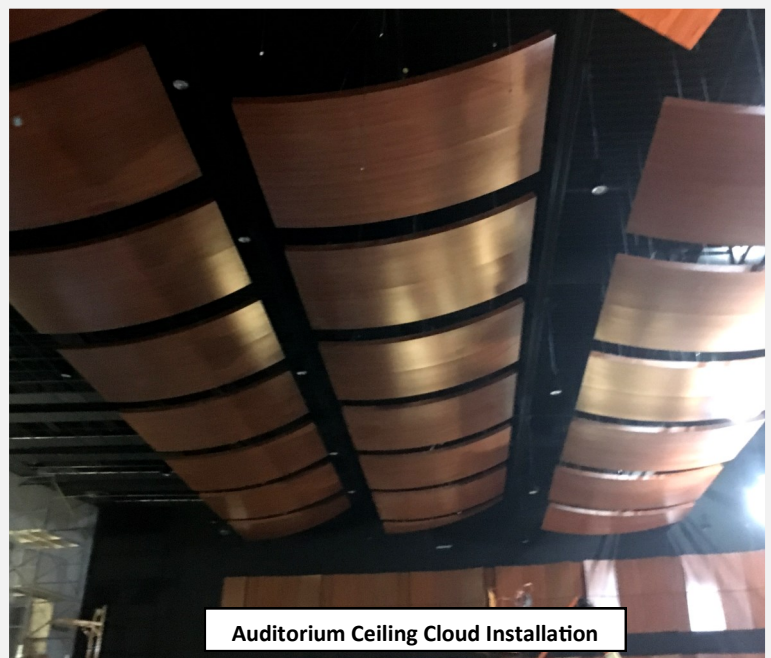

Auditorium Ceiling Cloud Installation
