



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

March 30th, 2018



CGSCHMIDT<sup>INC.</sup>

## SAFETY:

**Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.**

## MILESTONE DATES:

- May 18<sup>th</sup>: Gym Occupancy
- Summer 18<sup>th</sup>: Complete parking lot top coat
- Summer 18<sup>th</sup>: Commons / Tech Ed / Joe 2 Go
- September 4<sup>th</sup>: 1st Day of School

## PROGRESS THIS WEEK:

### Auditorium Addition (3/17 - 3/18)

- Remainder of interior metal panel has been installed
- TV in lobby has been installed
- Completion of punchlist items are ongoing

### Gym Addition (4/17 - 6/18)

- Wood floor stain installation is ongoing
- Installation of ceiling clouds and finishes are ongoing
- Painting of commons ceilings are complete
- Epoxy floors are complete in locker rooms

## GOALS NEXT 2 WEEKS:

### Auditorium Addition (3/6 - 3/18)


- Prep for Gala event on 4/7/18
- Lighting and sound commissioning

### Gym Addition (4/17 - 6/18)

- Installation of exterior metal panel will continue
- Glass and metal panel install on connectors
- Sanding, painting, and sealing gym floor
- MEP and architectural finishes (painting, flooring, etc.) will continue to be ongoing



Laying of CMU Wall Progress at PLTW

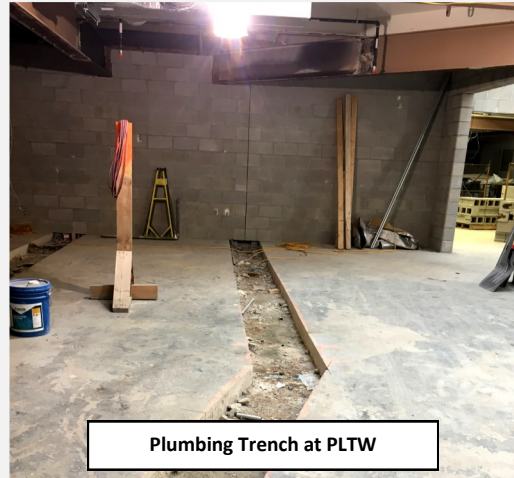

Plumbing Trench at PLTW



Gym Floor Installation Progress
