



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

April 13th, 2017



CGSCHMIDT^{INC.}

SAFETY:

As construction for the new auditorium addition and remodeling areas begin, please review the **NEW** emergency egress plans. Be aware that starting March 6th, 2017, doors 3, 4, and 5 will no longer be entry or exit paths until further notice.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- South fire wall is complete
- Mason began construction on the east elevation interior walls
- Demolition of the front vestibule is in progress
- Relocation of water main mobilization will take place on Friday and Saturday to begin work next week.

2nd Floor South Renovation (3/17 - 8/17)

- Butters Fetting started investigating disconnects & controls to be removed later on as construction activities advance
- Architectural demo (doors, flooring, etc.)

Tennis Courts

- Installation of fencing privacy slats will begin early next week.

GOALS NEXT 2

Auditorium Addition (3/6 - 12/17)

- Plumbers will work on the interior portion of the water main relocation
- Continue pouring interior foundation walls

Gym Addition (4/17—6/18)

- Erect construction fence in preparation for excavation
- Temporary walkway will be set in place for pedestrians

2nd Floor South Renovation (3/17 - 8/17)

- HVAC contractor will start removing VAV boxes.
- Demo (3) stairways in the art room

2nd Floor West Renovation (4/17 - 8/17)

- Interior abatement
- Install temporary partitions




Auditorium South Fire Wall



Auditorium Footings



Front Vestibule Demo

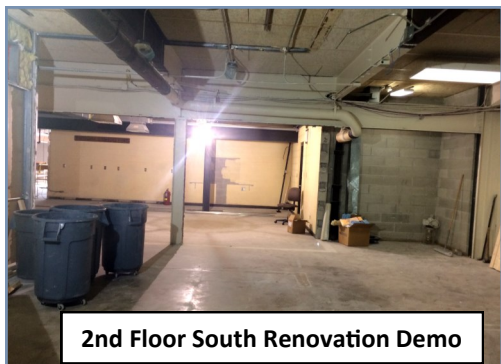

2nd Floor South Renovation Demo

MILESTONE DATES:

- 4/17: Install Tennis Court Fencing
- 9/17: Auditorium Addition Enclosure
- 7/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat
