



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

April 20th, 2017



CGSCHMIDT^{INC.}

SAFETY:

As construction for the new auditorium addition and remodeling areas begin, please review the **NEW** emergency egress plans. Be aware that starting March 6th, 2017, doors 3, 4, and 5 will no longer be entry or exit paths until further notice.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Mason started building the exterior east wall
- Orchestra pit excavation will be complete by the end of the week
- Demolition of the front vestibule is in progress
- Relocation of water main is in progress

2nd Floor South Renovation (3/17 - 8/17)

- Butters Fetting started investigating disconnects & controls to be removed later on as construction activities advance
- Architectural demo (doors, flooring, etc.)

Gym Addition (4-17 - 6/18)

- Construction fencing has been installed
- Stripping and preparing pad has started
- Temporary walkway has been set in place



Auditorium South East Corner Masonry



Auditorium Footings

GOALS NEXT 2

Auditorium Addition (3/6 - 12/17)

- Mason will continue to build interior masonry walls
- Continue pouring interior foundation walls

Gym Addition (4/17 - 6/18)

- Install required storm water provisions
- Excavation for gym foundation

2nd Floor South Renovation (3/17 - 8/17)


- HVAC contractor will remove VAV boxes.
- Demo (3) stairways in the art room

2nd Floor West Renovation (4/17 - 8/17)

- Interior abatement
- Install temporary partitions
- Architectural demo (ceiling, doors, etc.)



2nd Floor Abatement

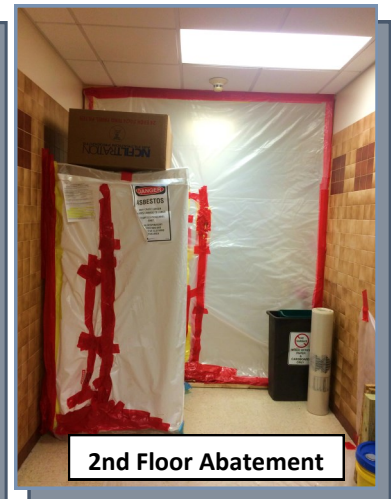

2nd Floor Abatement

MILESTONE DATES:

- 9/17: Auditorium Addition Enclosure
- 7/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat
