



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 1st, 2017



CGSCHMIDT^{INC.}

SAFETY:

As construction for the new auditorium addition and remodeling areas begin, please review the **NEW** emergency egress plans. Be aware that starting March 6th, 2017, doors 3, 4, and 5 will no longer be entry or exit paths until further notice.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Masons continue to finish interior masonry walls
- Installation of precast deadmen to begin this week

2nd Floor Renovation (3/17 - 8/17)

- All major demo has been completed
- Commonlinks continues installing stud framing and beginning drywall
- Above ceiling rough-ins is in progress

Gym Addition (4/17 - 6/18)

- Pouring of foundation footings continues
- Underground plumbing is underway along firewall

Library Renovation (6/17 - 8/17)

- Partial demo of walls, floors, and ceilings has begun

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Mason will finish building interior office masonry walls
- Precast installation will begin next week

Gym Addition (4/17 - 6/18)

- Continuing pouring footings

2nd Floor Renovation (3/17 - 8/17)

- Insulation removal above corridor ceilings will begin after last day of school

1st Floor Renovation (6/17 - 8/17)

- Partial demo will continue

MILESTONE DATES:


- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat



Auditorium Foundation Wall Form



Gym Footing Placement

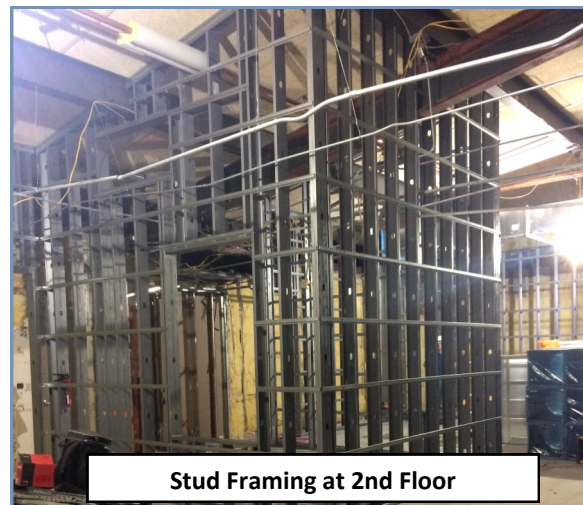

Stud Framing at 2nd Floor
