



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 7th, 2018



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

MILESTONE DATES:

- Summer 18': Complete parking lot top coat
- Summer 18': Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

PROGRESS THIS WEEK:

New Commons/Servery (3/18 –8/18)

- Block walls are complete at the servery
- Wall framing is ongoing
- Electrical wall rough-ins is ongoing
- Sprinkler rough-ins is in progress
- Installation of supply and return duct is ongoing

Tech Ed (5/18—8/18)

- 80% of wall demolition has been complete
- Saw cutting for underground electrical to occur by the end of the week
- Demolition of mechanical, electrical, and plumbing components is ongoing
- Underground work

Foods Classroom Remodel (6/18—8/18)

- Demolition of walls & MEP equipment started this week

GOALS NEXT 2 WEEKS:

New Commons/Servery (3/18—8/18)


- MEP rough-ins installation Wall framing
- Demolition of existing kitchen/prep and existing stairs
- Framing of skylights

Tech Ed (5/18—8/18)

- Demo will continue
- Pouring of foundations for the areas that were saw cut to occur next Tuesday
- Masonry walls to start next week

Foods Classroom Remodel (6/18—8/18)

- New door frames installation
- Masonry doors and corners
- MEP rough-ins

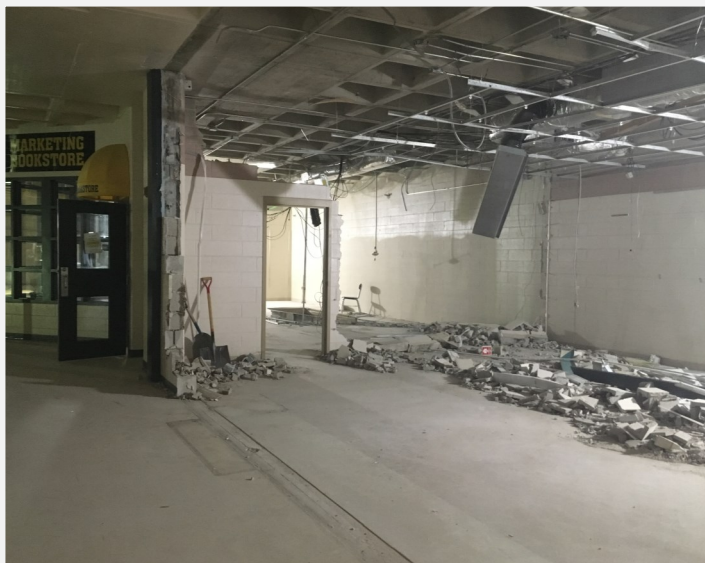

Bookstore & Classroom Wall Demolition



Servery/Commons Progress



Demolition Progress at Existing Commons
