



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 22nd, 2018



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

New Commons/Servery (3/18 –8/18)


- Wall framing is ongoing
- Installation of drywall is ongoing
- Electrical wall rough-ins is ongoing
- Sprinkler rough-ins is in progress
- Installation of supply and return duct is ongoing

Tech Ed (5/18—8/18)

- Masonry walls are ongoing
- Saw cutting for underground electrical is complete
- Demolition of mechanical, electrical, and plumbing components is ongoing
- Pouring of slab on grade
- Framing of walls to start at the end of the week

Foods Classroom Remodel (6/18—8/18)

- Installation of new door frames to start this week
- Underground plumbing work is ongoing

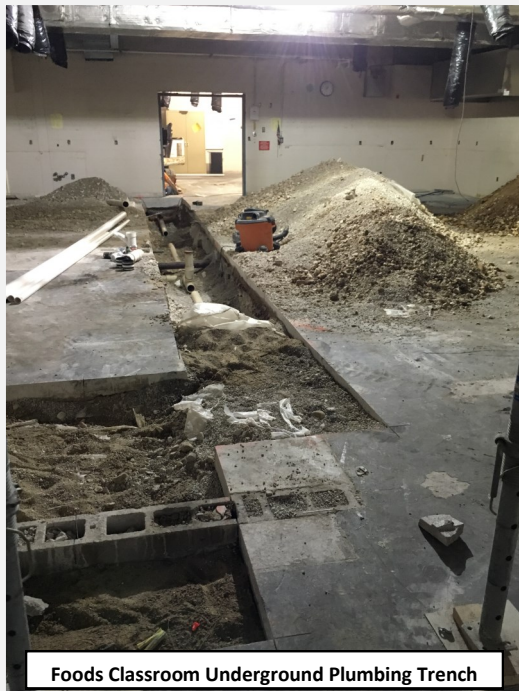

Foods Classroom Underground Plumbing Trench

MILESTONE DATES:

- Summer 18': Complete parking lot top coat
- Summer 18': Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

GOALS NEXT 2 WEEKS:

New Commons/Servery (3/18—8/18)

- MEP rough-ins
- Drywall and taping
- Framing of skylights

Tech Ed (5/18—8/18)

- Demo to be complete
- Masonry walls to continue
- Electrical wall and ceiling rough-ins
- Mechanical equipment rough ins

Foods Classroom Remodel (6/18—8/18)

- Masonry doors and corners
- MEP rough-ins



Servery/Commons Drywall



CMU Block for Commons Foam Seating
