



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

July 20th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Starting on 6/19, public access to the high school will only be available through the far west entrance during summer activities.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Mason continues to work on finishing the masonry walls at the mechanical room
- Deck detailing will be complete by the end of the week

2nd Floor West Renovation (3/17 - 8/17)

- Drywall installation is expected to be complete by the end of the week
- Tape and finishing of drywall will take place through the middle of next week
- Last few door frames have arrived onsite and will finish installation of all door frames

2nd Floor East Renovation (3/17 - 8/17)

- Electrical inspection is scheduled to take place on Friday
- Drywall installation is underway and is expected to be complete by the end of the week

Gym Addition (4/17 - 6/18)

- Long-span joists installation has been complete
- Deck fastening will be complete by the end of the week

Library Renovation (6/17 - 8/17)

- Installation of masonry walls is complete
- Saw cutting of the floor for underground electrical was completed
- MEP rough-ins continue

1st Floor Art Room Renovation (6/17 - 8/17)

- Demolition continues

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roof work to begin next week in the music room and mechanical room areas
- Precast braces to be removed in the upcoming weeks
- Foundation of the seating area to be poured mid next week

Gym Addition (4/17 - 6/18)

- Precast bracing will be removed following the removal of auditorium precast bracing
- Slab on grade to be poured after precast braces have been removed

2nd Floor West Renovation (3/17 - 8/17)

- Tape and finish drywall work will be complete by next week
- Painter will begin block filling next week

2nd Floor East Renovation (3/17 - 8/17)

- Tape and finishing of drywall will begin

Library Renovation (6/17 - 8/17)

- Underground electrical work to begin next week
- Installation of drywall ceilings and soffits to begin next week after electrical inspection
- Painting of block and frames to begin next week

MILESTONE DATES:


- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat



Auditorium—Area C Joists Installation



2nd Floor—West Side Ready for Painting

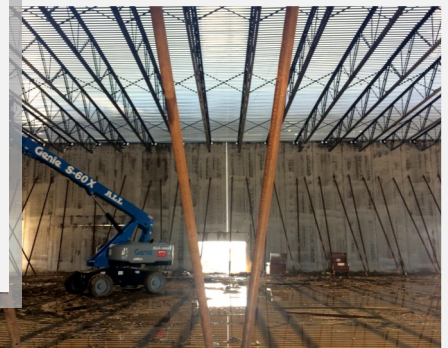

Gym Steel Deck Completion
