



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

July 27th, 2017



CGSCHMIDT<sup>INC.</sup>

## SAFETY:

**Starting on 6/19, public access to the high school will only be available through the far west entrance during summer activities.**

## PROGRESS THIS WEEK:

### Auditorium Addition (3/6 - 12/17)

- Masons continue to work on load bearing walls
- Installation of structural steel continues and is expected to be complete by the end of the week

### 2nd Floor West Renovation (3/17 - 8/17)

- Drywall, tape, and finish is expected to be complete by the end of the week
- Last few borrowed lite frames have arrived onsite and will finish installation of all borrowed lite frames
- Painting will begin by the end of the week

### 2nd Floor East Renovation (3/17 - 8/17)

- Tape and finish of drywall continues

### Gym Addition (4/17 - 6/18)

- Masons have started construction of masonry walls

### Library Renovation (6/17 - 8/17)

- Drywall installation taping continues to be underway
- Underground electrical work is ongoing

## GOALS NEXT 2 WEEKS:

### Auditorium Addition (3/6 - 12/17)

- Installation of joist and deck in Area A to begin next week
- Stage concrete to be poured next week

### Gym Addition (4/17 - 6/18)

- Precast bracing will be removed following the removal of auditorium precast bracing
- Slab on grade to be poured after precast braces have been removed

### 2nd Floor West Renovation (3/17 - 8/17)

- Painting of walls, ceilings, and door frames will continue
- Skylight openings to be cut next week
- Ceiling grid installations expected to begin next week
- Wall protection is expected to arrive on site next week to begin installation

### 2nd Floor East Renovation (3/17 - 8/17)

- Tape and finishing of drywall will continue

### Library Renovation (6/17 - 8/17)


- Painting of block and frames to begin next week

## MILESTONE DATES:

- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Auditorium Steel Erection Progress

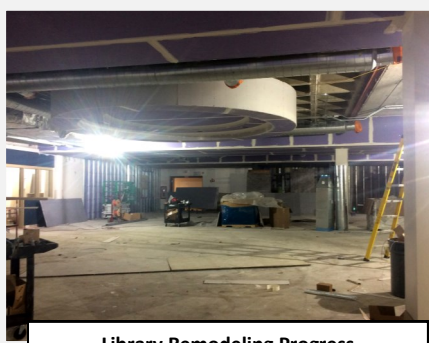

Library Remodeling Progress



Gym Exterior Walls Progress
