



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

September 21, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Roof blocking at the main auditorium to be complete by the end of the week
- Wall framing at auditorium lobby continues
- Exterior stud framing and sheathing is ongoing
- Smaller roofing activities surrounding the main auditorium are ongoing
- Seat risers are in progress
- MEP rough in activities continue

2nd Floor East Renovation (3/17 - 8/17)

- Ceiling grid installation began this week
- Light fixtures installation expected to commence at the end of the week

Gym Addition (4/17 - 6/18)

- Framing of the soffits started this week
- Electrical rough-ins have started this week
- Slab on grade has been poured

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will continue throughout the rest of the auditorium
- Exterior framing and sheathing will continue
- Slab on grade for the bowl itself will be poured next week
- Interior walls within the auditorium will be framed

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing expected to begin within the next couple weeks
- Exterior opening blocking to begin next week
- Slab on grade at the lobby is expected to be poured next week

2nd Floor East Renovation (3/17 - 8/17)

- Ceiling grid installation will continue to be ongoing
- Elevator replacement activities will be ongoing
- Electrical inspection is expected to occur next week
- Overhead doors are expected to arrive onsite next week for installation

MILESTONE DATES:


- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Exterior Framing



Office Area Wall Framing

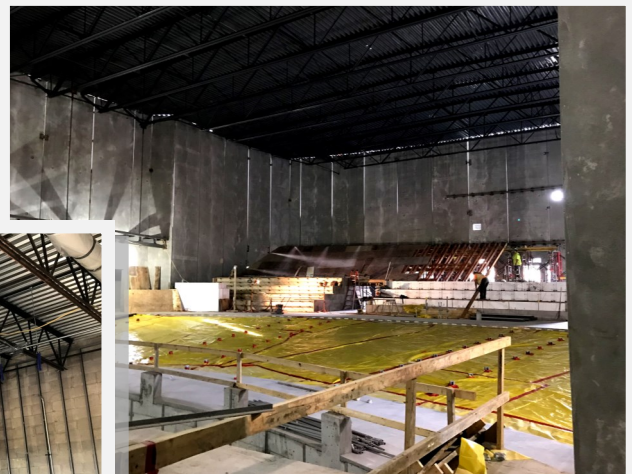

Auditorium Seating Progress
