



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

October 5th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Roof at the new offices area is ongoing
- Mechanical mezzanine and stage craft slab have been poured
- Wall framing at auditorium lobby continues
- Exterior metal panel installation began at the east side this week
- Laying of brick is ongoing from east to west
- Seat risers are in progress
- MEP rough in activities continue

2nd Floor East Renovation (3/17 - 8/17)

- Paint touch ups will be ongoing
- Carpet installation is ongoing

Gym Addition (4/17 - 6/18)

- Framing of the soffits continue
- Structural framing is ongoing
- MEP rough-ins in joists continue
- Mechanical mezzanine has been poured

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will be complete by next week
- Seating risers will continue to be poured next week
- Drywall installation will begin next week
- Fire protection activities will begin next week in the offices area

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs work to begin in the next couple weeks
- Slab on grade finishing activities will begin next week

2nd Floor East Renovation (3/17 - 8/17)


- Elevator replacement inspection is scheduled next Friday
- Carpet flooring installation will continue

MILESTONE DATES:

- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Gym Corridor

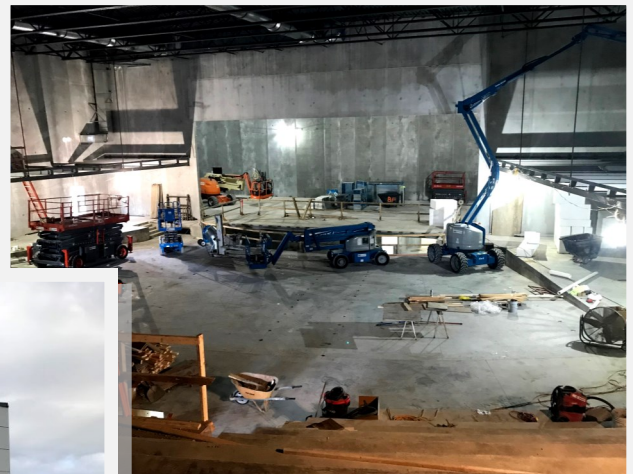

Auditorium Seating Progress



Metal Panel Installation on East Side of Auditorium
