



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

October 12th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- 2nd section of seat risers will be poured on Friday
- Spiral stairs have been installed
- Mechanical rough-ins above ceiling is in progress
- Wall framing at auditorium lobby continues
- Exterior metal panel installation continues
- Laying of brick continues
- Roofers to return this week to finish the rest of the lower roofs, weather permitting

2nd Floor East Renovation (3/17 - 8/17)

- Paint touch ups will be ongoing
- Carpet and LVT floor installation is complete
- Final cleaning will begin Friday

Gym Addition (4/17 - 6/18)

- Framing of the soffits continue
- Structural framing is ongoing
- MEP rough-ins in joists continue

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will be complete by next week
- Seating risers will continue to be poured next week
- Drywall installation will begin next week
- Glazing framing will begin next week

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs work to begin in the next couple weeks
- Slab on grade finishing activities will begin next week

2nd Floor East Renovation (3/17 - 8/17)

- Elevator replacement inspection is re-scheduled for next week
- Punchlist items will be complete within the next couple of weeks

MILESTONE DATES:


- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Metal Panel Installation in Auditorium



Spiral Stairs in Auditorium

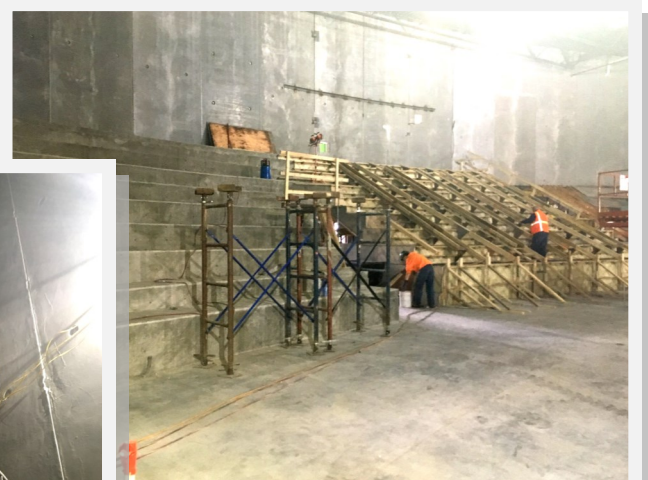

Auditorium Seating Progress
