



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

October 19th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Last section of seat risers to be poured by the end of the week
- Catwalk and lighting platforms installation is ongoing
- Mechanical rough-ins above ceiling is in progress
- Wall framing at auditorium lobby continues
- Exterior metal panel installation continues
- Roofing work continues to be finalized

2nd Floor East Renovation (3/17 - 8/17)

- Paint touch ups will be ongoing
- Punchlist has been performed and issued to the trades
- Elevator inspection has been successfully completed

Gym Addition (4/17 - 6/18)

- Framing of the soffits continue
- Roof blocking is ongoing
- Sprinkler system piping has been hung
- MEP rough-ins in joists continue

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will be complete by next week
- Drywall installation will begin soon after building enclosure
- Glazing framing will begin next week

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs work to begin in the next couple weeks
- Slab on grade finishing activities will begin next week

2nd Floor East Renovation (3/17 - 8/17)


- Punchlist items will be complete by the end of next week

MILESTONE DATES:

- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Gym Addition Exterior Sheathing

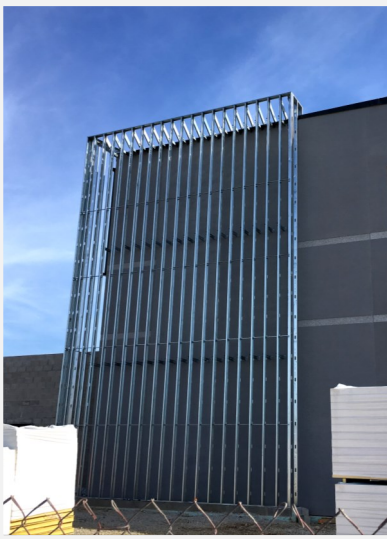

Gym Metal Panel Framing—West Elevation



Auditorium Interior Framing
