



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

November 9th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Temporary heat has been put in place
- Painting in the music wing will be complete this week
- Installation of sprinklers is ongoing
- Cleaning up of raised concrete seating forms is ongoing
- Above ceiling work is in progress
- Wall framing at auditorium lobby continues
- Exterior metal panel installation continues
- Installation of windows is ongoing

Gym Addition (4/17 - 6/18)

- Remainder of roofs continue to be installed
- Masonry walls installation at locker rooms continue
- Roof blocking is expected to be complete this week
- MEP rough-ins in joists continue
- Exterior foam insulation continues

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Ceiling grid installation is expected to begin next week in the music wing and corridors
- Drywall installation will begin soon after building enclosure
- Interior framing and drywall installation will continue

Gym Addition (4/17 - 6/18)


- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs work will continue
- Lobby concrete slab will be poured next week
- Storefront field check measurements will be taking place in the next couple weeks
- Connectors between the existing building and new gym will be put in place in the next couple weeks

MILESTONE DATES:

- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Auditorium Enclosure Progress

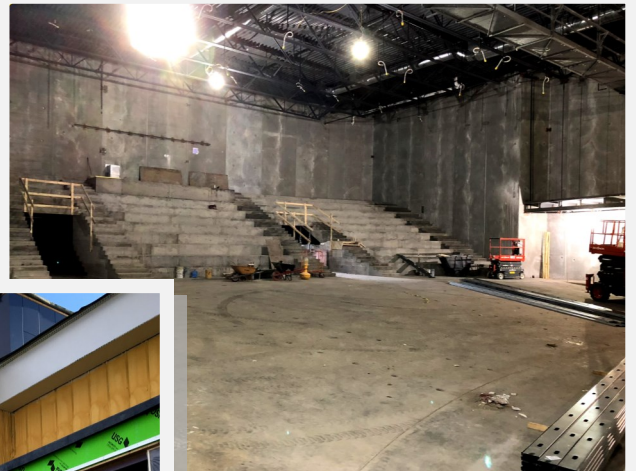

Raised Seating Completed



Auditorium Metal Panel Installation Progress
