



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

December 7th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Flooring installation in band room is complete. Orchestra and choir rooms are in progress.
- Installation of sound doors in practice rooms is ongoing.
- Ceiling tile installation has been completed in the music wing
- Air handling units startup will begin today at the offices
- Installation of lighting fixtures will continue
- Exterior metal panel installation continues
- Installation of glazing is ongoing
- Exterior brick installation is ongoing

Gym Addition (4/17 - 6/18)

- Above ceiling rough-ins will continue
- Exterior brick installation will continue
- Exterior metal panel installation at the courtyard is ongoing
- Connectors between the existing building and the new gym is in progress

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Wall panels installation will be ongoing
- Flooring installation will continue throughout next week
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will continue
- Glazing installation will continue
- Ceiling clouds installation in the main auditorium will begin in a couple weeks

Gym Addition (4/17 - 6/18)

- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Interior brick installation will begin next week
- Connectors between the existing building and new gym will be put in place in the next couple weeks

MILESTONE DATES:


- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Ensemble Room Progress



New Offices Corridor

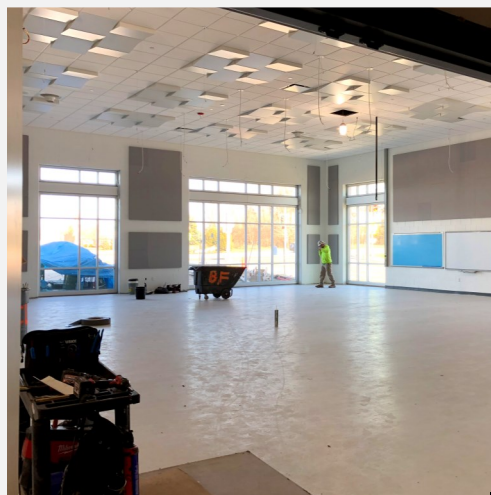

New Band Room Progress
