



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

December 28th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school. The current main entrance will not be available for use starting on January 2nd. All students and staff to use the new main entrance.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- New front entrance will be complete by the end of the week
- Carpet at the attendance/reception area will be complete by the end of the week
- Installation of transaction window at the attendance office will be complete by the end of the week
- Installation of glazing and storefront is complete
- Final occupancy walkthrough inspection has been complete
- Temporary partition will be installed by the end of the week to separate the ongoing construction area from the new finished entrance/lobby areas
- Painting of auditorium stage is ongoing
- Installation of plywood for wall paneling is ongoing

Gym Addition (4/17 - 6/18)

- Wall framing in locker rooms is ongoing
- Above ceiling rough-ins will continue
- Connectors between the existing building and the new gym is in progress

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)


- Wall panels installation will resume weather permitting
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will continue in main auditorium
- Ceiling clouds installation in the main auditorium will begin in a couple weeks

Gym Addition (4/17 - 6/18)


- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Connectors between the existing building and new gym will continue

MILESTONE DATES:


- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat

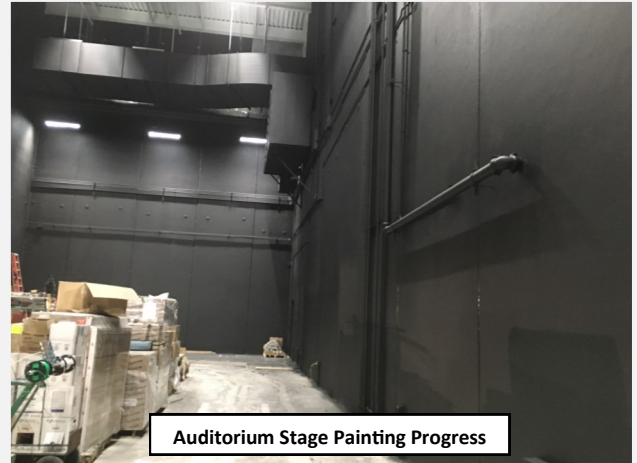

Auditorium Stage Painting Progress

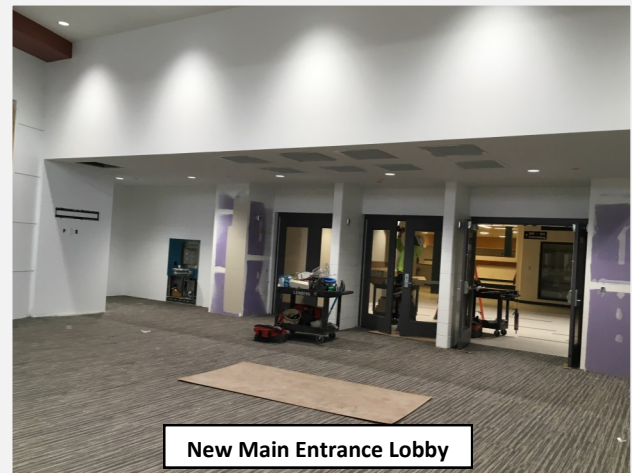

New Main Entrance Lobby

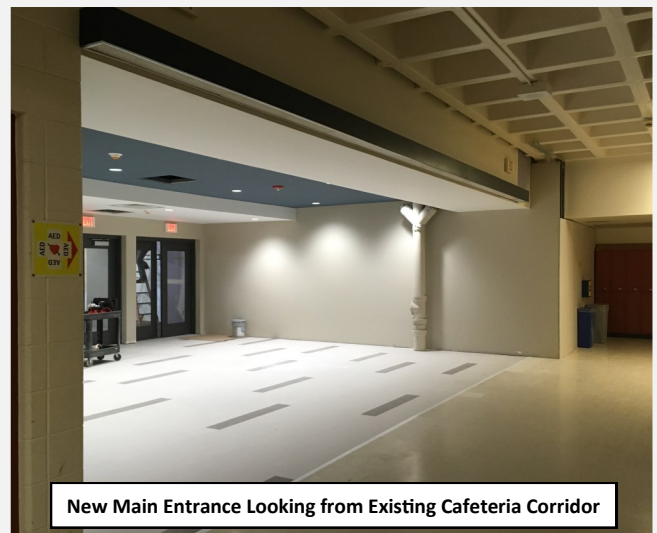

New Main Entrance Looking from Existing Cafeteria Corridor
