



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

January 18th, 2018



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school. The current main entrance will not be available for use starting on January 2nd. All students and staff to use the new main entrance.

MILESTONE DATES:

- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 3/18)

- Wood wall panels installation is ongoing
- Ceiling clouds installation is ongoing
- Theatrical rigging installation started this week
- Taping and finishing of lobby walls is ongoing

Gym Addition (4/17 - 6/18)

- Wall framing at lobby is in progress
- Framing of locker benches will be complete
- Ceilings and walls will be painted by the end of the weekend
- Gym equipment is expected to arrive onsite by the end of the week

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 3/18)

- Exterior wall panels installation will resume weather permitting
- Drywall, taping, and finishing in the lobby and north corridors will be ongoing
- Auditorium wall panels will continue
- Theatrical rigging preparation will be ongoing
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will continue in main auditorium
- Ceiling clouds installation in the main auditorium will continue

Gym Addition (4/17 - 6/18)


- Concrete to be poured at locker benches expected next week
- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Connectors between the existing building and new gym will continue



Gym Progress



Gym Locker Room Bench Framing

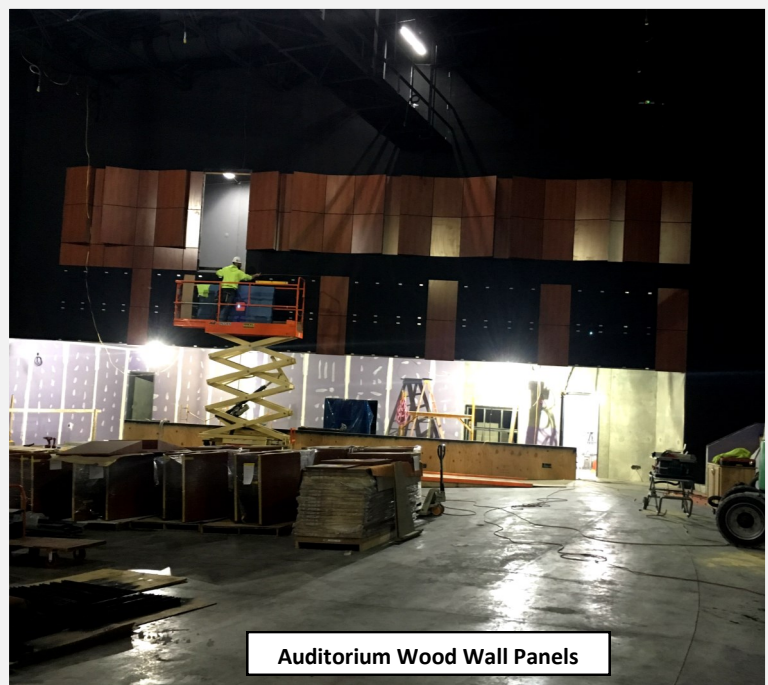

Auditorium Wood Wall Panels
