



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling  
May 17h, 2018



## SAFETY:

**Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.**

## PROGRESS THIS WEEK:

### Gym Addition (4/17 - 6/18)

- Flooring at connectors is near complete
- Wall images installation is complete
- Final cleaning started this week
- Glass installation at connectors is near complete
- Above ceiling inspection is complete

### New Commons/Servery (3/18 –8/18)

- Installation of stairways is ongoing
- Installation of masonry wall is ongoing
- Wall framing is ongoing

## MILESTONE DATES:

- May 18<sup>th</sup>: Gym Occupancy
- Summer 18<sup>th</sup>: Complete parking lot top coat
- Summer 18<sup>th</sup>: Commons / Tech Ed / Joe 2 Go
- September 4<sup>th</sup>: 1st Day of School

## GOALS NEXT 2 WEEKS:

### Gym Addition (4/17 - 6/18)


- Installation of backordered interior metal panels will be complete in a few weeks once material arrives onsite
- Final inspection is scheduled next week
- Punchlist walkthrough is scheduled for next week

### New Commons/Servery (3/18—8/18)

- MEP rough-ins installation will continue
- Installation of stairwell walls will be ongoing
- Wall framing to be ongoing



Masonry Stairs at Servery Progress

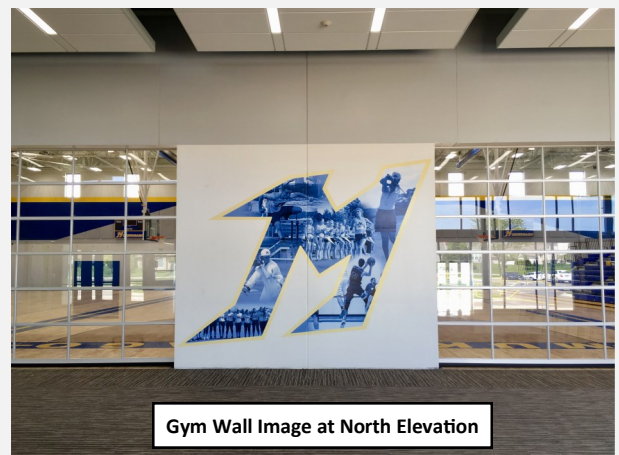

Gym Wall Image at North Elevation



Gym Wall Image at West Elevation
