



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

May 25th, 2017



CGSCHMIDT^{INC.}

SAFETY:

As construction for the new auditorium addition and remodeling areas begin, please review the **NEW** emergency egress plans. Be aware that starting March 6th, 2017, doors 3, 4, and 5 will no longer be entry or exit paths until further notice.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Backfill of orchestra pit will take place Thursday and Friday.
- Orchestra pit foundation walls have been complete
- Masons continue to finish interior masonry walls
- Installation of precast deadmen to begin on Friday

2nd Floor Renovation (3/17 - 8/17)

- All major demo has been completed
- Commonlinks has begun installing metal studs for drywall

Gym Addition (4/17 - 6/18)

- Pouring of foundation footings continues
- Pouring of foundation walls will begin by the end of the week
- Construction fence was installed and temporary walkway was established in place

Library Renovation (6/17 - 8/17)

- Partial demo of walls, floors, and ceilings has begun

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Mason will continue to build interior masonry walls
- Installation of precast deadmen will continue next week

Gym Addition (4/17 - 6/18)

- Continuing pouring footings
- Forming and pouring foundation walls
- Underground plumbing along firewall

2nd Floor Renovation (3/17 - 8/17)

- Insulation removal above corridor ceilings will begin after last day of school
- Drywall installation to begin next week

1st Floor Renovation (6/17 - 8/17)

- Partial demo will continue

MILESTONE DATES:


- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat



Auditorium Formwork & Rebar



Gym Footings Formwork

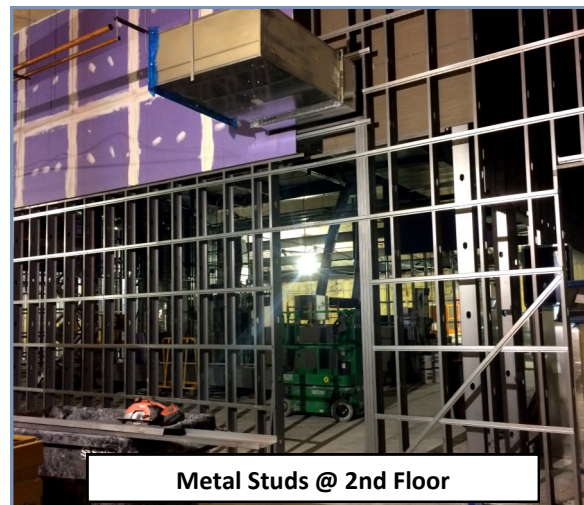

Metal Studs @ 2nd Floor
