



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling
May 31st, 2018



SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Tech Ed (5/18—8/18)

- Demolition of walls is ongoing
- Demolition of mechanical, electrical, and plumbing components is ongoing

New Commons/Servery (3/18 –8/18)

- Block walls installation is near complete
- Wall framing is ongoing
- Toilet partitions installation in the restrooms across the new commons are complete

MILESTONE DATES:

- May 18th: Gym Occupancy
- Summer 18th: Complete parking lot top coat
- Summer 18th: Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

GOALS NEXT 2 WEEKS:

Tech Ed (5/18—8/18)


- Demo will continue
- Saw cutting for underground foundations and electrical
- Underground work

New Commons/Servery (3/18—8/18)

- MEP rough-ins installation Wall framing
- Demolition of existing kitchen/prep and existing stairs
- Masonry door openings to wrap up next week
- Framing of skylights



PLTW Construction Progress

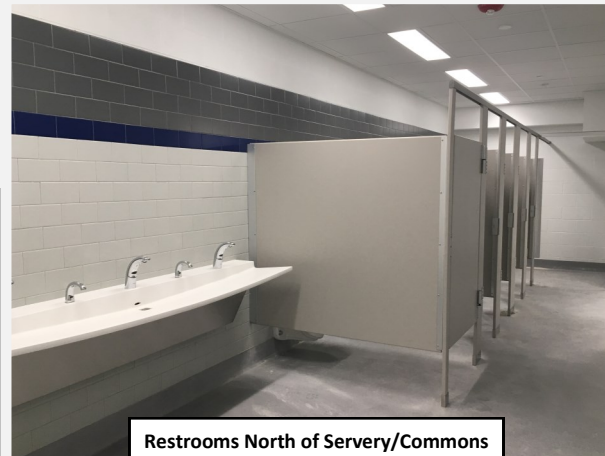

Restrooms North of Servery/Commons



Lecture Hall
