



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 8th, 2017



CGSCHMIDT INC.

SAFETY:

Starting on 6/19, public access to the high school will only be available through the far west entrance during summer activities.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Precast panels have shown up onsite for installation this week
- Masons will continue building masonry walls at the office area of the addition

2nd Floor Renovation (3/17 - 8/17)

- Commonlinks continues installing stud framing
- Above ceiling MEP rough-ins are in progress
- Installation of drywall has begun

Gym Addition (4/17 - 6/18)

- Footings and foundation walls will be complete by the end of the week

Library Renovation (6/17 - 8/17)

- Partition walls will be set up in place for demolition to start next week

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Installation of precast panels will continue
- Masons will continue to work in the office area of addition

Gym Addition (4/17 - 6/18)

- Installation of masonry walls will begin

2nd Floor Renovation (3/17 - 8/17)


- Major demolition of walls and finishes will begin next week

1st Floor Renovation (6/17 - 8/17)

- Demolition in library will begin next week

MILESTONE DATES:


- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lots top coat

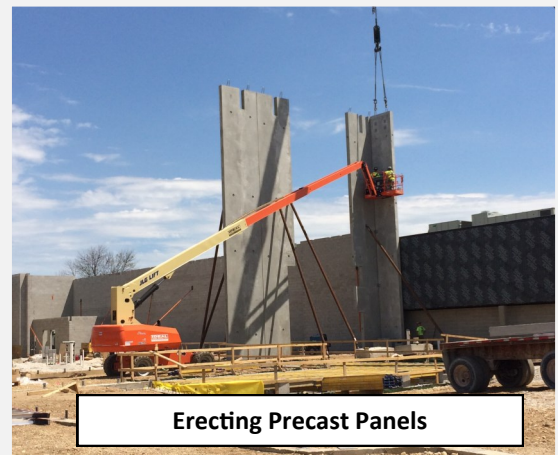

Erecting Precast Panels



Pouring Concrete at Gym South Wall

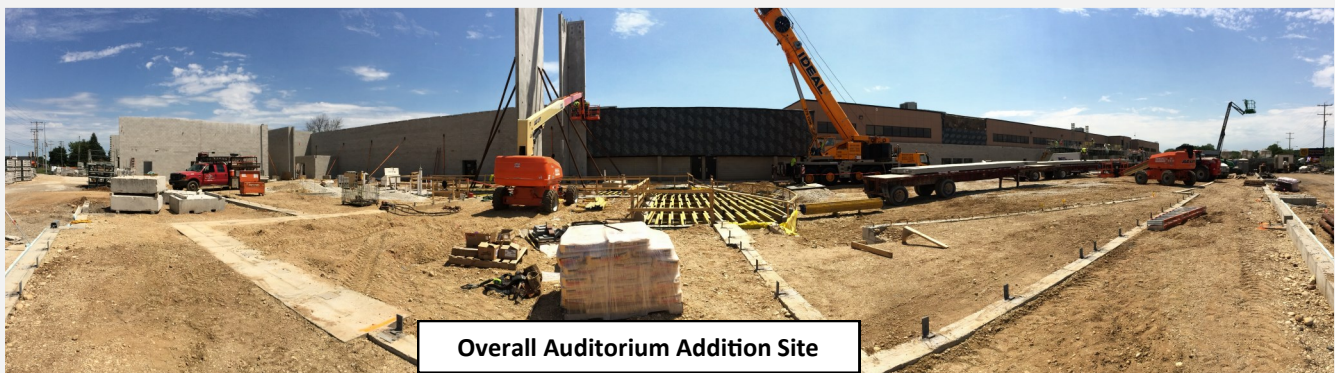

Overall Auditorium Addition Site
