



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 15th, 2018



CGSCHMIDT<sup>INC.</sup>

## SAFETY:

**Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.**

## MILESTONE DATES:

- Summer 18': Complete parking lot top coat
- Summer 18': Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

## PROGRESS THIS WEEK:

### New Commons/Servery (3/18 –8/18)

- Wall framing is ongoing
- Electrical wall rough-ins is ongoing
- Sprinkler rough-ins is in progress
- Installation of supply and return duct is ongoing
- Demolition of existing kitchen/prep and existing stairs is ongoing

### Tech Ed (5/18—8/18)

- 80% of wall demolition has been complete
- Saw cutting for underground electrical is complete
- Demolition of mechanical, electrical, and plumbing components is ongoing
- Pouring of slab on grade
- Framing of walls to start at the end of the week

### Foods Classroom Remodel (6/18—8/18)

- Installation of new door frames to start this week

## GOALS NEXT 2 WEEKS:

### New Commons/Servery (3/18—8/18)


- MEP rough-ins installation
- Wall framing
- Framing of skylights

### Tech Ed (5/18—8/18)

- Demo will continue
- Pouring of foundations for the areas that were saw cut to occur next Tuesday
- Masonry walls to start next week

### Foods Classroom Remodel (6/18—8/18)

- Masonry doors and corners
- MEP rough-ins

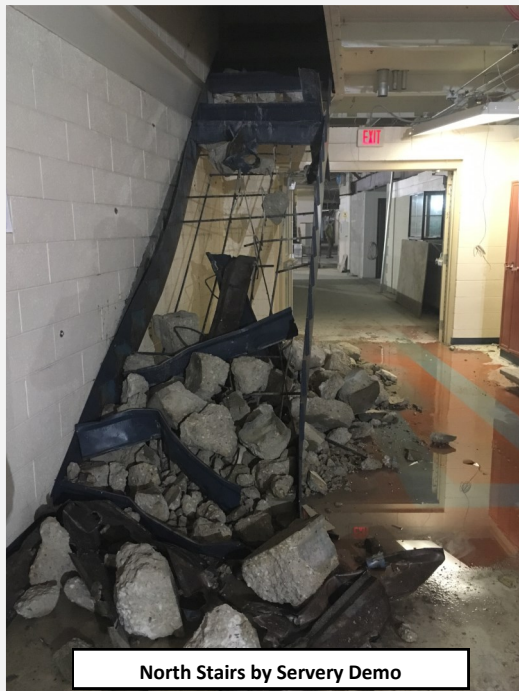

North Stairs by Servery Demo



Servery/Commons Demo Progress



Pouring of Footings for South Corridor Addition
