



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

June 28th, 2018



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

New Commons/Servery (3/18 –8/18)

- Wall framing is ongoing
- Drywall taping is ongoing at the servery area
- Electrical wall rough-ins is ongoing
- Framing of skylights and soffits is ongoing
- Above ceiling rough-ins are ongoing

Tech Ed (5/18—8/18)

- Masonry walls are near complete
- MEP rough-ins are ongoing
- Demolition of mechanical, electrical, and plumbing components is ongoing
- Drywall taping is ongoing

Foods Classroom Remodel (6/18—8/18)

- Underground plumbing work is complete
- Plumbing rough-ins is ongoing



Tech Ed—Woods Progress

MILESTONE DATES:

- Summer 18': Complete parking lot top coat
- Summer 18': Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

GOALS NEXT 2 WEEKS:

New Commons/Servery (3/18—8/18)

- MEP rough-ins
- Painting
- Framing of skylights

Tech Ed (5/18—8/18)


- Masonry walls to finish
- MEP wall and ceiling rough-ins
- Painting to start next week

Foods Classroom Remodel (6/18—8/18)

- Masonry doors and corners
- MEP rough-ins



Art Gallery Wall Framing

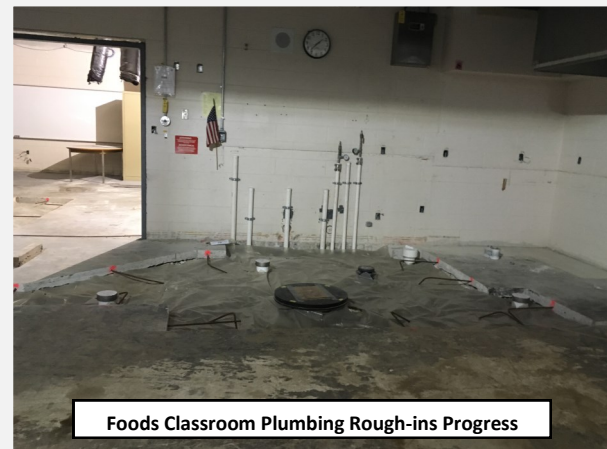

Foods Classroom Plumbing Rough-ins Progress
