



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

July 5th, 2018



CGSCHMIDT<sup>INC</sup>

## SAFETY:

**Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.**

## PROGRESS THIS WEEK:

### New Commons/Servery (3/18 –8/18)

- Kitchen hoods have been installed
- Drywall taping is ongoing at the servery area
- Electrical wall rough-ins is ongoing
- Framing of skylights and soffits is ongoing
- Above ceiling rough-ins are ongoing

### Tech Ed (5/18—8/18)

- Masonry walls are near complete
- MEP rough-ins are ongoing
- Drywall taping is near complete

### Foods Classroom Remodel (6/18—8/18)

## MILESTONE DATES:

- Summer 18': Complete parking lot top coat
- Summer 18': Commons / Tech Ed / Joe 2 Go
- September 4th: 1st Day of School

## GOALS NEXT 2 WEEKS:

### New Commons/Servery (3/18—8/18)

- MEP rough-ins
- Installation of kitchen ceilings
- Installation of drywall at Joe2Go
- Soffits at commons

### Tech Ed (5/18—8/18)


- Infill of interior masonry walls
- Exterior masonry walls
- MEP wall and ceiling rough-ins
- Painting to start next week

### Foods Classroom Remodel (6/18—8/18)


- Ceiling grid installation



Tech Ed Progress: Metals/Manufacturing

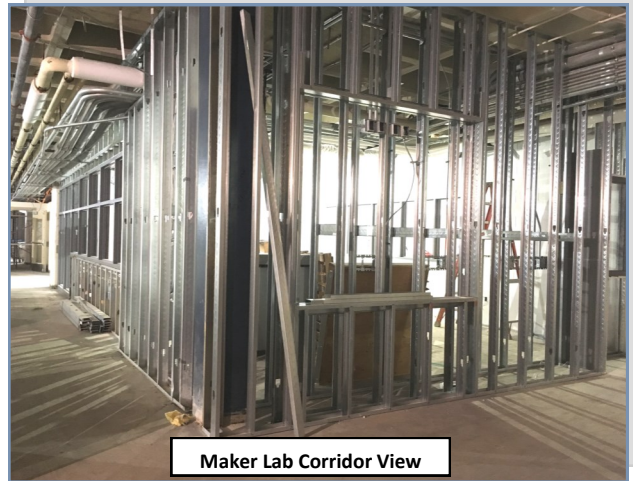

Maker Lab Corridor View

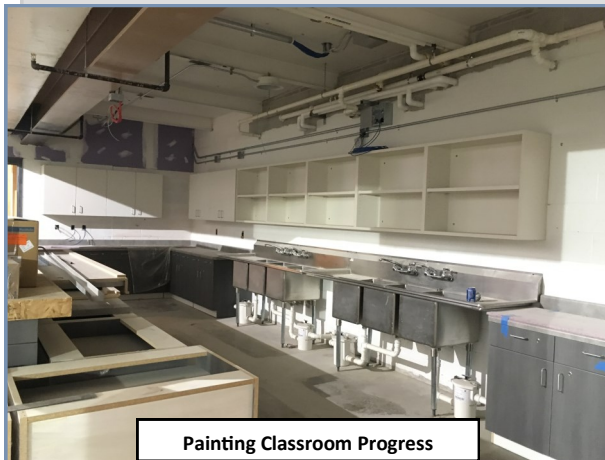

Painting Classroom Progress



IT Branding Progress
