



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling
September 8th, 2017



SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Roof decking is complete in Area A
- Roof blocking is ongoing
- Wall framing continues
- Exterior stud framing and sheathing is ongoing
- Pouring of concrete floors throughout the auditorium to begin later in the week
- Seat risers are in progress
- MEP rough in activities continue

2nd Floor East Renovation (3/17 - 8/17)

- Tape and finish of drywall continues
- Above ceiling electrical piping and wiring is ongoing
- Existing elevator demolition work has been complete for the replacement of existing elevator

Gym Addition (4/17 - 6/18)

- Iron workers continue working on the detailing of decking
- Roofing work continues

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Roofing work will continue throughout the rest of the auditorium
- Exterior framing and sheathing will continue
- Slab on grade for the bowl itself will be poured next week

Gym Addition (4/17 - 6/18)

- Slab on grade is expected to be poured late next week
- Roof is expected to be complete next week
- Above ceiling rough-ins are expected to begin next week

2nd Floor East Renovation (3/17 - 8/17)

- Tape and finishing of drywall will be complete
- Ceiling grid installation is expected to begin next week
- New opening for the replacement of existing elevator will occur next couple weeks

COMPLETED REMODELED AREAS:


- Punchlist items will be ongoing and expected to be complete in a couple weeks

MILESTONE DATES:

- 9/17: Auditorium Addition Enclosure
- 10/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Auditorium Exterior Sheathing

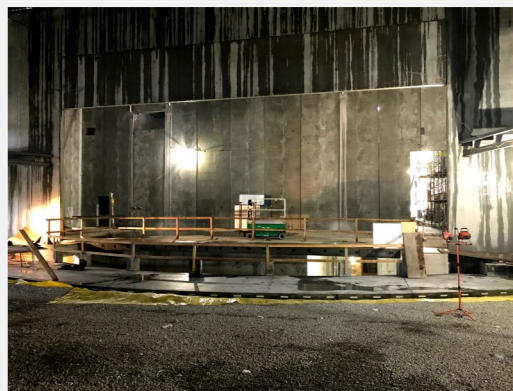

Auditorium Stage



Auditorium Seat Risers
