



CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

November 16th, 2017



CGSCHMIDT^{INC.}

SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

PROGRESS THIS WEEK:

Auditorium Addition (3/6 - 12/17)

- Ceiling grid installation in the music area is ongoing
- Installation of lighting fixtures began earlier this week
- Installation of sprinklers is ongoing
- The fire protection deluge system has been installed in the auditorium stage
- Drywall installation at auditorium lobby continues
- Exterior metal panel installation continues
- Installation of glazing is ongoing

Gym Addition (4/17 - 6/18)

- Exterior metal panel installation began this week
- Masonry walls installation at locker rooms continue
- Glazing installation began this week
- Exterior foam insulation continues

GOALS NEXT 2 WEEKS:

Auditorium Addition (3/6 - 12/17)

- Ceiling grid installation to be ongoing for the next couple weeks
- Drywall installation will be complete in the next couple weeks
- Flooring installation to begin in the next couple weeks

Gym Addition (4/17 - 6/18)

- Temporary heat will be put in place early next week
- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Lower roofs will be complete in the next couple weeks
- Connectors between the existing building and new gym will be put in place in the next couple weeks

MILESTONE DATES:


- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Offices Glazing and Metal Panel



Men's & Women's Restrooms
Plumbing Rough-ins at New Gym

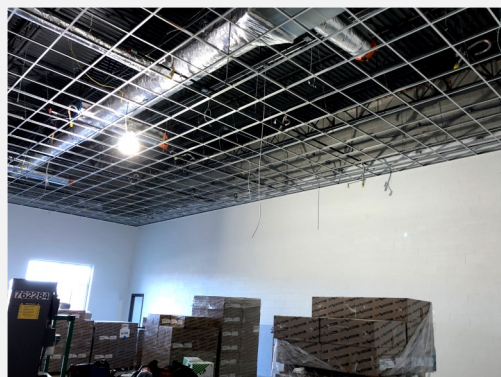

Ceiling Grid Installation in Music Area
