



# CONSTRUCTION UPDATE

Mukwonago High School—Additions & Remodeling

November 30th, 2017



CGSCHMIDT<sup>INC.</sup>

## SAFETY:

Please continue to be mindful of the restricted areas as construction activities continue, both outside and inside the school.

## PROGRESS THIS WEEK:

### Auditorium Addition (3/6 - 12/17)

- An above ceiling inspection is scheduled for this Friday in the music wing and offices/lobby
- Ceiling tile will be installed after above ceiling inspection is complete
- Installation of lighting fixtures will continue
- The fire protection deluge system has been installed in the auditorium stage
- Exterior metal panel installation continues
- Installation of glazing is ongoing
- Exterior brick installation is ongoing

### Gym Addition (4/17 - 6/18)

- Temporary heat has been put in place
- Exterior metal panel installation at the courtyard is ongoing
- Exterior concrete finishing patio is ongoing this week
- Connectors between the existing building and the new gym started this week
- Exterior foam insulation continues

## GOALS NEXT 2 WEEKS:

### Auditorium Addition (3/6 - 12/17)

- Ceiling tile installation to be ongoing for the next couple weeks
- Flooring installation to begin on Monday
- Ceiling finishes (light fixtures, sprinkler heads, etc.) will be installed next week

### Gym Addition (4/17 - 6/18)


- MEP rough in activities will continue
- Exterior framing and sheathing will continue
- Connectors between the existing building and new gym will be put in place in the next couple weeks

## MILESTONE DATES:


- 11/17: Auditorium Addition Enclosure
- 11/17: Gym Addition Enclosure
- 3/18: Auditorium Occupancy
- 5/18: Gym Occupancy
- Summer 18': Complete parking lot top coat



Auditorium Lobby Framing Progress

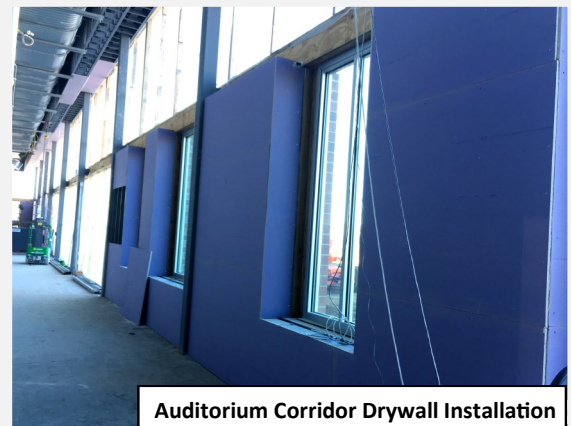

Auditorium Corridor Drywall Installation

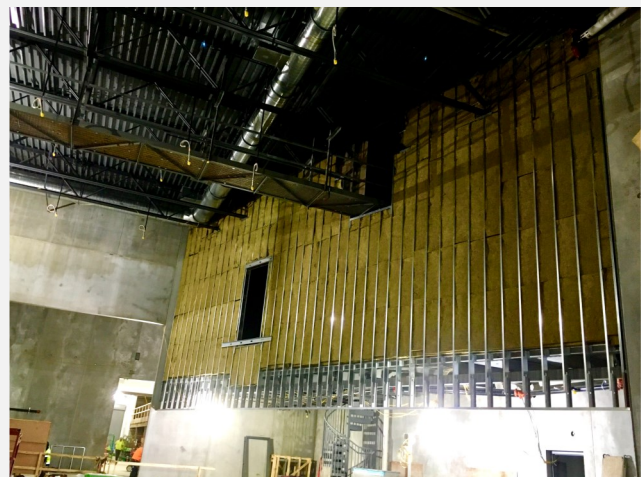

Auditorium Lighting Platform Framing Progress
